
Baseline Schedule - WBS Summary (stages & functions)

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.1	Project Milestones	
1.2	Stage 1 - Mobilization & Design (Month 1)	
1.2.1	Management & Mobilization	
1.2.2	Submittals (Contractor)	
1.2.3	SAR Reviews & Approvals	
1.2.4	Permits & Authority Approvals	
1.2.5	Survey & Assessment	
1.2.6	Design & Engineering	
1.2.7	Procurement & Logistics	
1.3	Stage 2 - Procurement & Construction (Months 2-10)	
1.3.1	Management & Mobilization	
1.3.2	Submittals (Contractor)	
1.3.3	SAR Reviews & Approvals	
1.3.4	Permits & Authority Approvals	
1.3.7	Procurement & Logistics	
1.3.8	Factory Acceptance Testing (FAT)	
1.3.9	Civil & Cable Works by Section (risk-ranked sequence)	
1.3.10	Station Power, Shelter, Systems, Cloud & Cyber Installation	
1.3.11	Testing, Commissioning & Validation	
1.3.13	Schedule Contingency (Time-Risk Allowance)	
1.4	Stage 3 - System Testing & Commissioning (Month 11)	
1.4.1	Management & Mobilization	
1.4.11	Testing, Commissioning & Validation	
1.4.12	Documentation, Training & Handover	
1.5	Stage 4 - Documentation & Handover (Month 12)	
1.5.2	Submittals (Contractor)	
1.5.3	SAR Reviews & Approvals	
1.5.12	Documentation, Training & Handover	
1.6	Post-Completion - Defects Liability Period (DLP)	

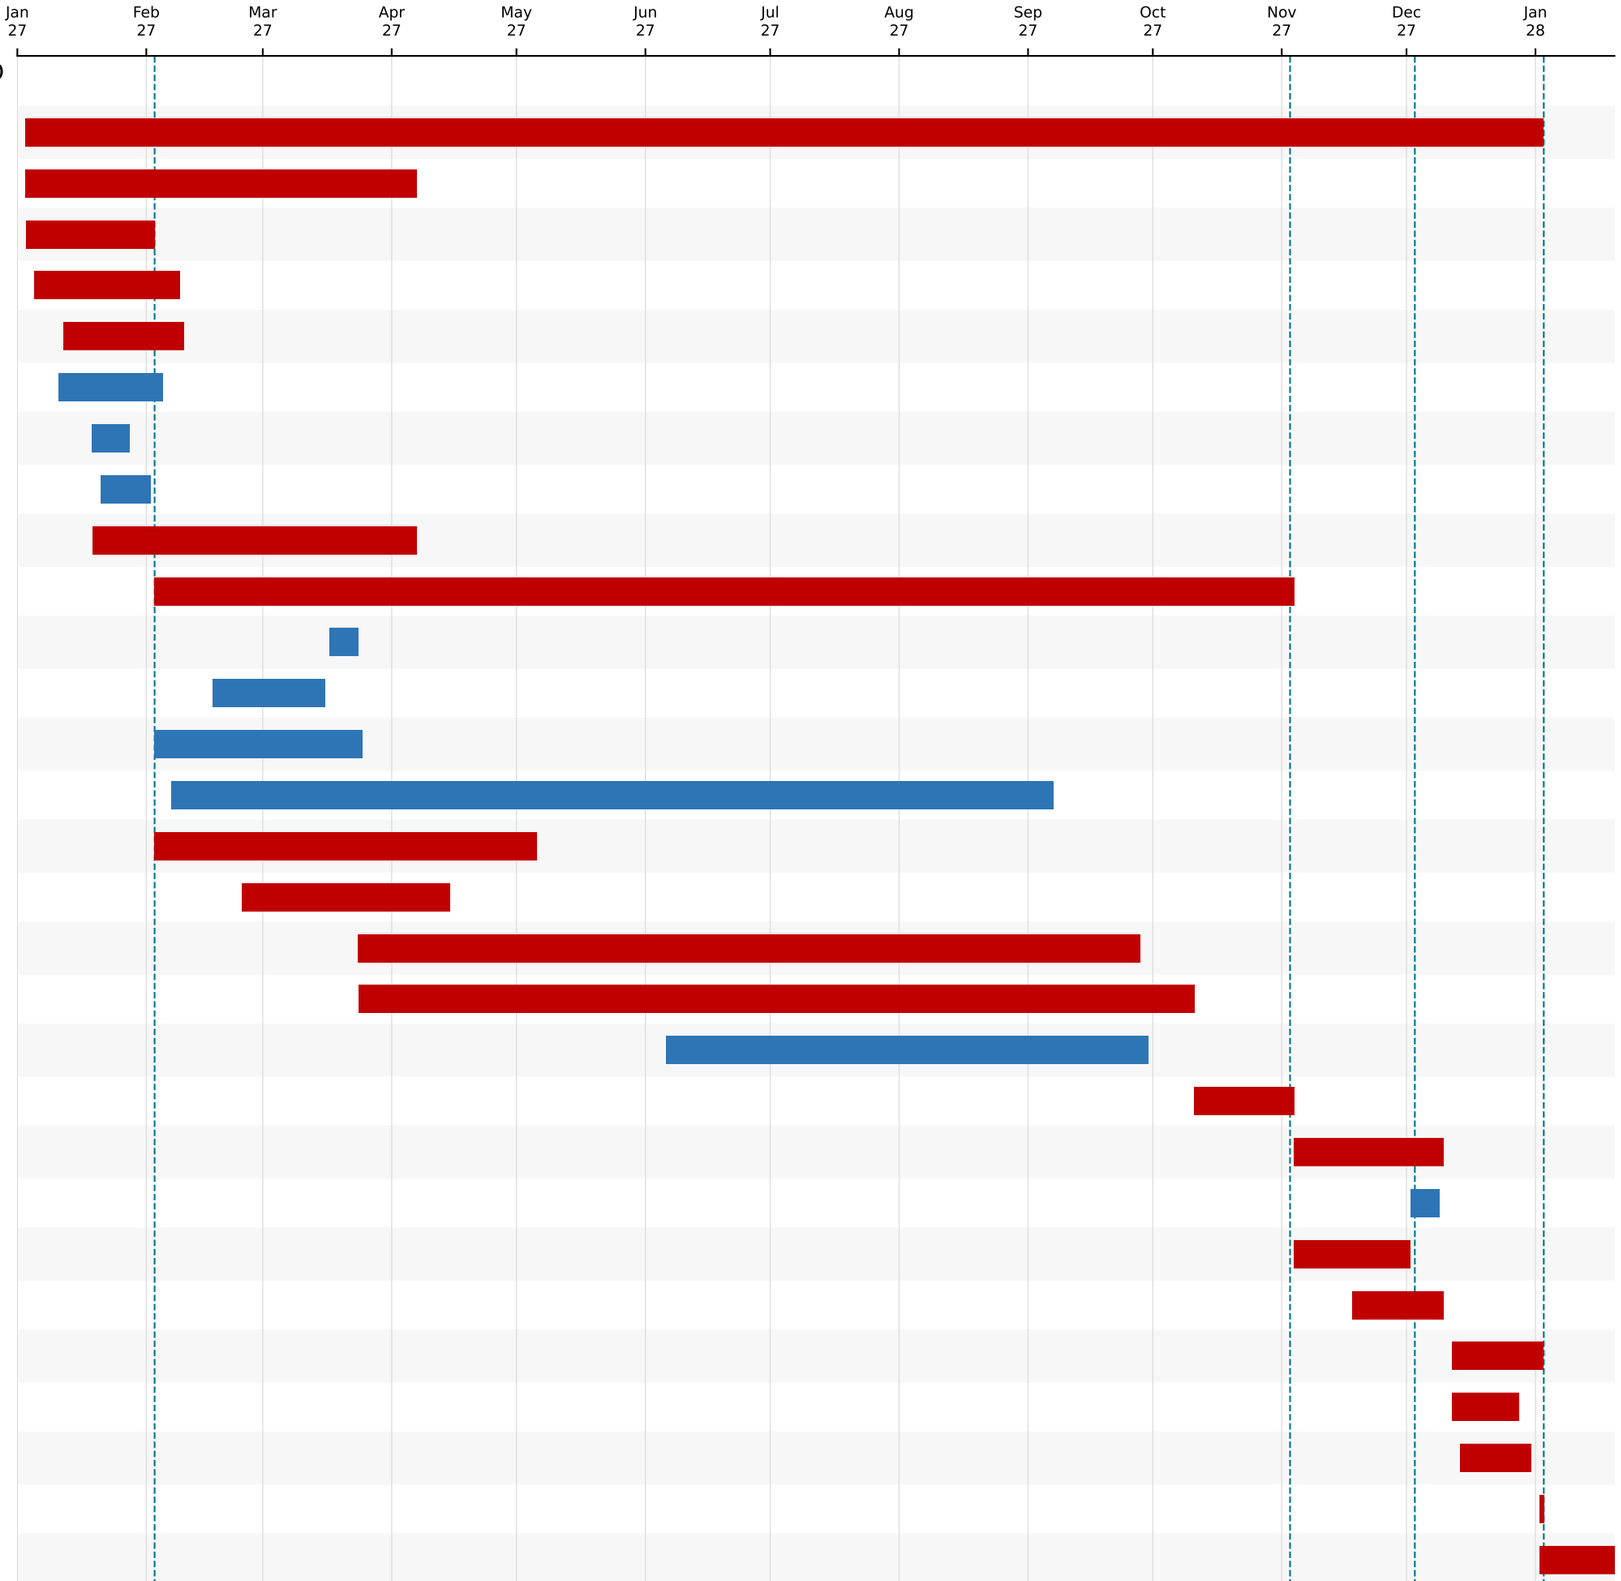


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.1 Project Milestones		
MS-001	NTP - Notice to Proceed (assumed date; re-base on actual NTP)	0
MS-WP01	WP-01 issued - site access for survey & assessment	16
MS-030	All material submittals approved	171
MS-010	Stage 1 complete - mobilization done & IFC package submitted	168
MS-020	IFC package approved	16
MS-WP02	WP-02 issued - route construction works	16
MS-WP04	WP-04 issued - station works	109
MS-WP03	WP-03 issued - track crossing & culvert works	29
MS-WP05	WP-05 issued - testing & commissioning	148
MS-060	FAT complete (all equipment groups)	122
MS-050	All long-lead materials delivered to site	107
MS-070	Stage 2 complete - procurement, construction & installation complete	0
MS-080	SAT complete (incl. integration tests & cyber audit closure)	0
MS-100	Stage 3 complete - commissioning & performance validation complete	0
MS-120	Taking-Over - CONTRACT COMPLETION (12 months from NTP)	0
1.2.1 Management & Mobilization		
MOB-1010	Kick-off meeting & project management set-up	0
MGT-1060	Project management, QA/QC & HSE supervision and records (LOE)	
MGT-1070	Weekly & monthly progress reporting (LOE)	
MGT-1090	Obtain SAR risk scores & confirm Section priority (SAR input)	25
MOB-1030	PTS training & PO induction - batch 1 (initial team)	17
MOB-1020	Insurance (CAR / TPL) & performance bond issuance	16
MOB-1080	Protection Officer on site during all field works (LOE)	
MOB-1040	Site establishment - offices & temporary facilities	44
MOB-1050	Site security, fencing & traffic management (LOE)	
MOB-3005	PTS training & PO induction - batch 2 (field crews)	41
1.2.2 Submittals (Contractor)		
SUB-1410	QA/QC Plan, HSE Plan & Project Execution Plan - prepare & submit	50
SUB-1430	Material submittal - DSS cable NZS-DSS-C02, 48-core FO cable, TDR c...	0
SUB-1450	Material submittal - FO closures, handholes/manholes, steel & rigid...	44
SUB-1440	Material submittal - TDR system, weather station, comms modules/SIM...	30
SUB-1420	Method statements & ITPs (survey, trenching, cable laying, OTDR/spl...	37
SUB-1535	Address SAR comments & resubmit cable materials	0
SUB-1490	FAT procedures & test plans (TDR, cables, weather, comms, UPS, clou...	30
SUB-1480	Interface Control Document - existing 1.5 km system & iSiteCentral	138
SUB-1470	Cybersecurity (NCA ECC-1/CSCC-1/OTCC-1, SAR OT/ICS) & local-cloud a...	85
DSN-1320	IFC package QA check & submission to SAR	16
1.2.3 SAR Reviews & Approvals		
APR-1550	SAR review & approval - civil materials (closures, handholes, condu...	44
APR-1510	SAR review & approval - QA/QC, HSE & Execution Plans	50
APR-1530	SAR review - cable materials (DSS, FO, TDR coax)	0
APR-1540	SAR review & approval - equipment materials (TDR, weather, comms, U...	30
APR-1520	SAR review & approval - method statements & ITPs	37
APR-1536	SAR final approval - cable materials	0
APR-1660	SAR review & approval - FAT procedures (SAR witness notice incl.)	30

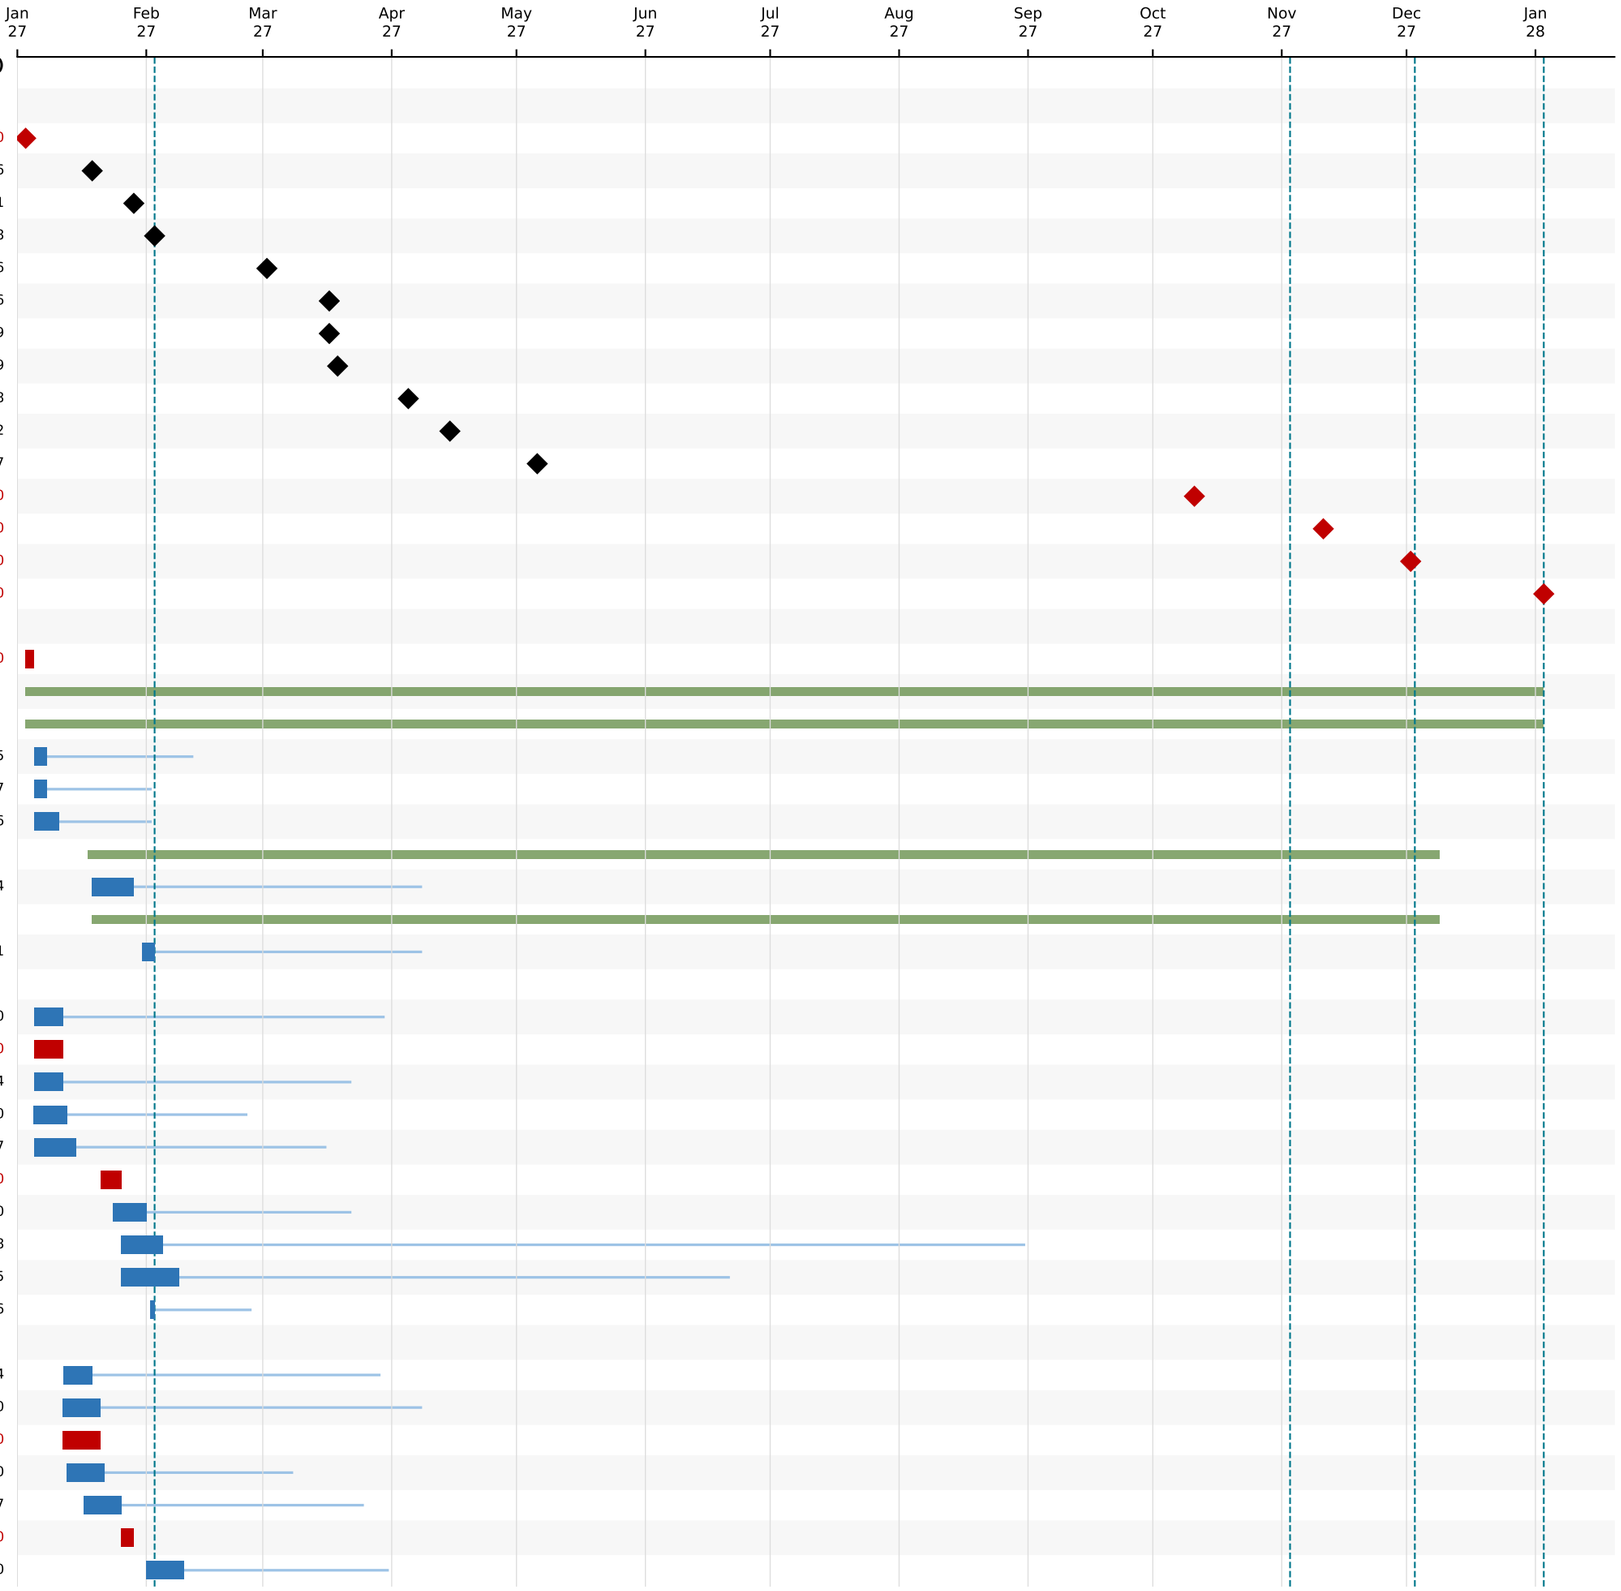


Critical path (TF = 0) · Non-critical (light line = total float) · Level of effort · Milestone · SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.2.4 Permits & Authority Approvals		
PRM-1110	Prepare & submit WP-01 request in Work Permit Portal (survey & asse...	16
PRM-1120	SAR review & issue WP-01 (Work Permit Portal)	16
PRM-2510	Request SIM / data-service activation from STC (primary & backup SIM)	158
PRM-2105	Prepare TTF02 / Delivery Plan, PICOP certificates & PTS card register	37
PRM-2520	STC SIM provisioning & activation	158
PRM-2410	Submit load / connection request to SEC for power upgrade (applicab...	125
1.2.5 Survey & Assessment		
SRV-1210	Existing system, power capacity & shelter assessment (incl. data co...	16
SRV-1220	Topographic survey, GPR utilities detection & dilapidation survey (...	16
1.2.6 Design & Engineering		
DSN-1310	Detailed engineering - route, cables, power & shelter (IFC drawings)	16
1.2.7 Procurement & Logistics		
PRC-CLS10	Place PO & supplier kick-off - FO closures, splice trays, connector...	44
PRC-CND10	Place PO & supplier kick-off - Steel & rigid conduits	51
PRC-HH10	Place PO & supplier kick-off - Handholes & manholes (precast)	46
PRC-MRK10	Place PO & supplier kick-off - Marker posts, warning tape & route m...	165
PRC-SND10	Arrange sweet-sand source, approval & stockpile at site	79
PRC-CND20	Manufacture / supply - Steel & rigid conduits	80
PRC-MRK20	Manufacture / supply - Marker posts, warning tape & route markers	244
PRC-HH20	Manufacture / supply - Handholes & manholes (precast)	73
PRC-CLS20	Manufacture / supply - FO closures, splice trays, connectors & pigt...	69
PRC-COM10	Place PO & supplier kick-off - Communication modules & SIM hardware	124
PRC-PWR10	Place PO & supplier kick-off - UPS (min. 4 h) & electrical panels	93
PRC-TDR10	Place PO & supplier kick-off - TDR system (interrogator, antenna & ...	85
PRC-WX10	Place PO & supplier kick-off - Weather station sensors	116
PRC-COM20	Manufacture / supply - Communication modules & SIM hardware	187
PRC-WX20	Manufacture / supply - Weather station sensors	175
PRC-PWR20	Manufacture / supply - UPS (min. 4 h) & electrical panels	144
PRC-TDR20	Manufacture / supply - TDR system (interrogator, antenna & accessor...	132
PRC-DSS10	Place PO & supplier kick-off - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-FO10	Place PO & supplier kick-off - Outdoor 48-core FO cable - DAS (5,50...	22
PRC-TDRC10	Place PO & supplier kick-off - TDR coaxial cable (5,500 LM)	39
1.3.1 Management & Mobilization		
MOB-3010	Mobilize plant, equipment & labour; compound & logistics set-up	16
1.3.2 Submittals (Contractor)		
SUB-1570	Address SAR comments & resubmit IFC package	16
SUB-1630	Address SAR comments & resubmit cyber/cloud design	85
SUB-1495	SAT, commissioning & performance-validation procedures	148
1.3.3 SAR Reviews & Approvals		
APR-1560	SAR review - IFC design package	16
APR-1650	SAR / system-owner review - Interface Control Document	138
APR-1620	SAR IT/OT & cybersecurity review - architecture design	85
APR-1580	SAR final approval - IFC package	16
APR-1640	SAR final approval - cyber/cloud design	85
APR-1670	SAR review & approval - SAT/commissioning procedures	148

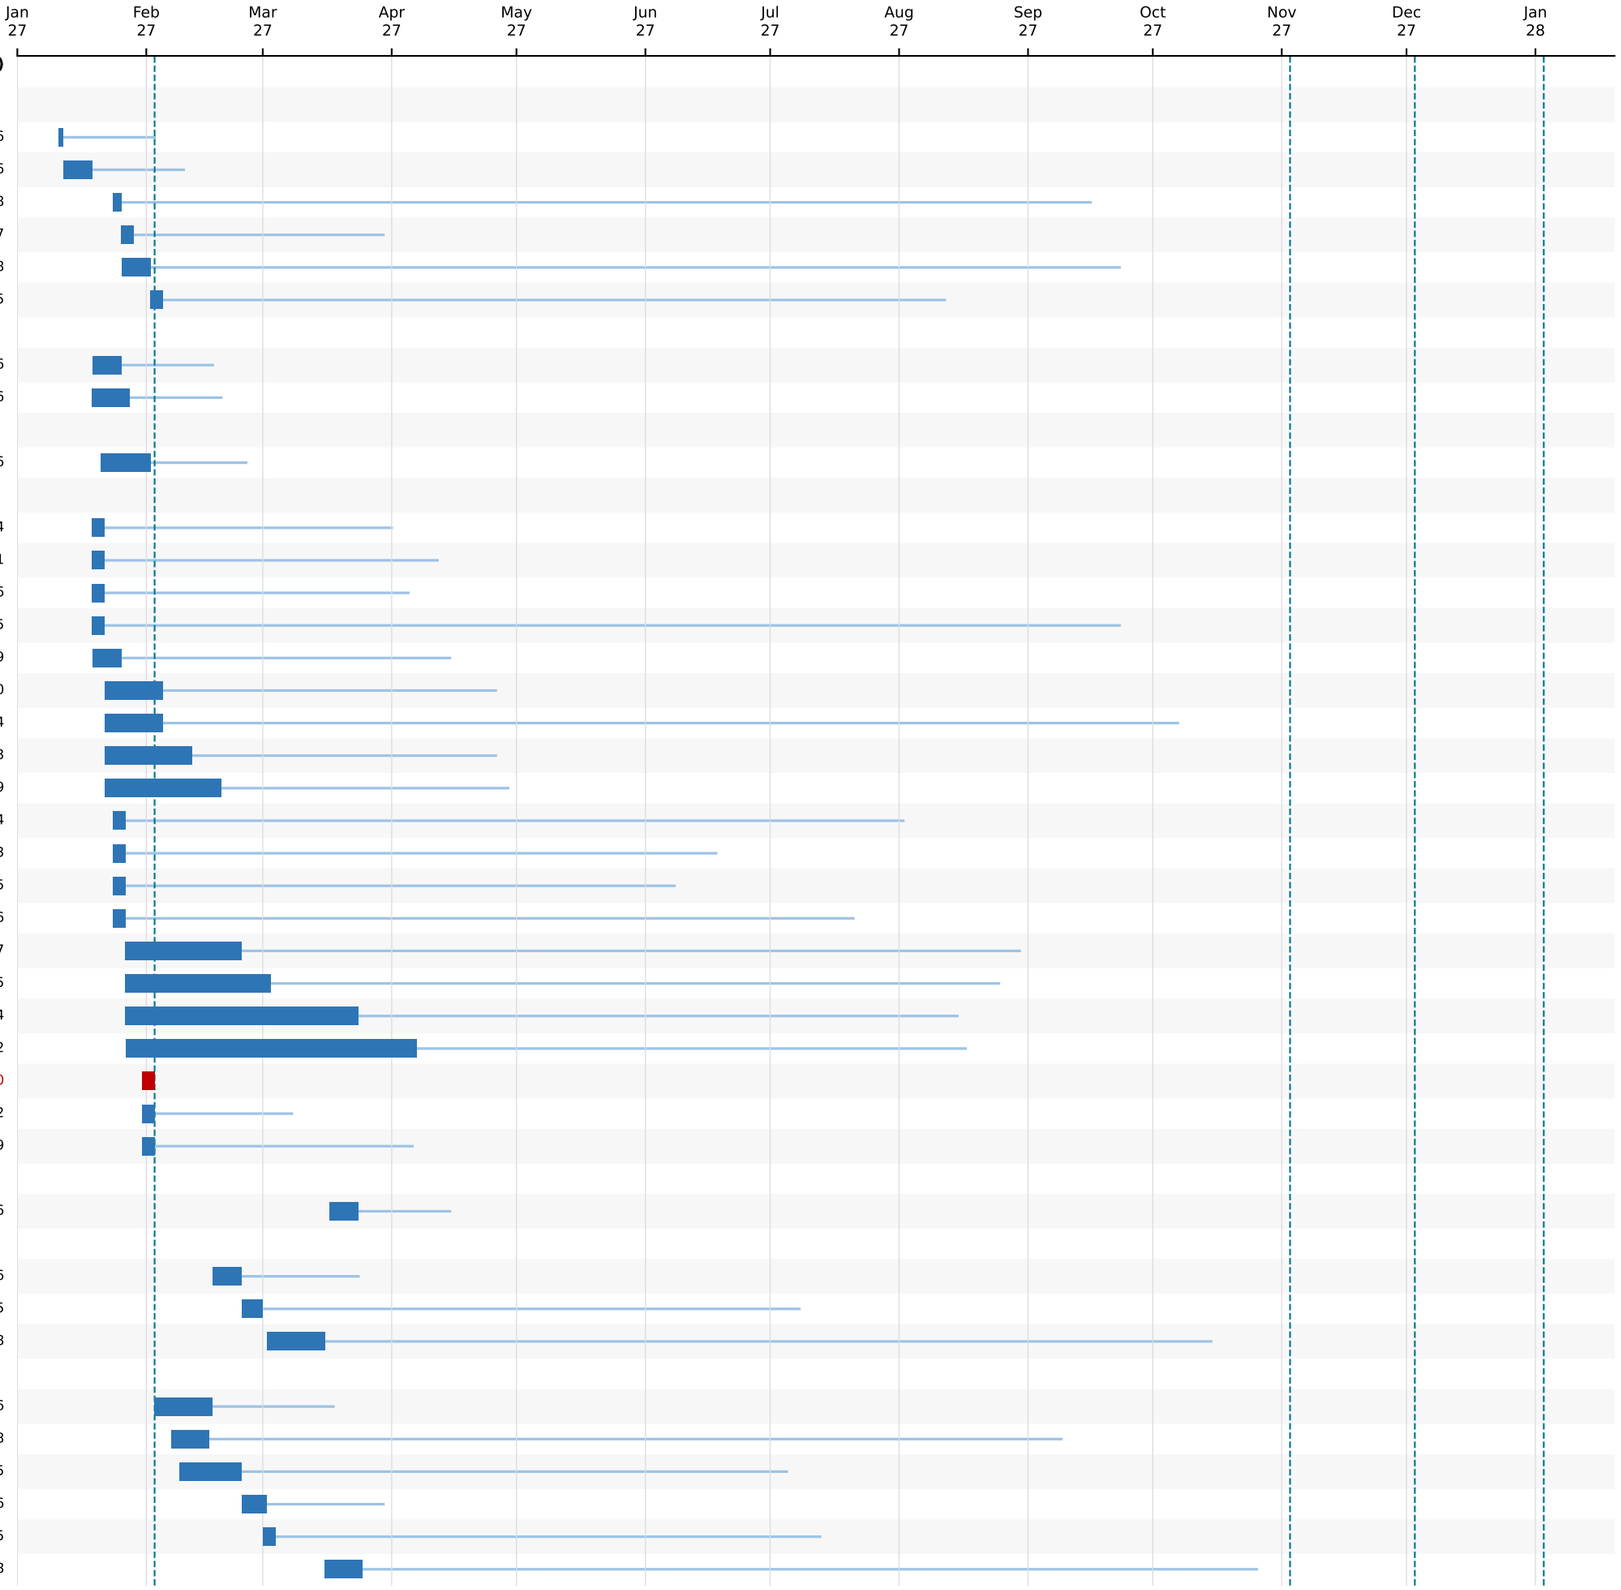


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.3.4	**Permits & Authority Approvals**	
PRM-2420	SEC review & connection approval (duration TBC)	125
PRM-2610	Request access / NOC & outage window - existing system & iSiteCentr...	138
PRM-2620	Owner NOC & agreed tie-in / outage window	138
PRM-2110	Prepare & submit WP-02 (route construction works, Sections 1-5) in ...	16
PRM-2210	Prepare & submit WP-03 (steel conduits at culverts & track crossing...	29
PRM-2310	Prepare & submit WP-04 (power, shelter & equipment works at monitor...	109
PRM-2120	SAR review & issue WP-02	16
PRM-2320	SAR review & issue WP-04	109
PRM-2220	SAR review & issue WP-03 (track crossings / possession)	29
PRM-3110	Prepare & submit WP-05 (testing, commissioning & live-system tie-in...	148
PRM-3120	SAR review & issue WP-05	148
PRM-2150	Permit extension 1 - progress report, updated insurance policy & TT...	23
PRM-2160	SAR review & approve permit extension 1	23
PRM-2170	Permit extension 2 - progress report, updated insurance policy & TT...	23
PRM-2180	SAR review & approve permit extension 2	23
1.3.7	**Procurement & Logistics**	
PRC-TDRC20	Manufacture / supply - TDR coaxial cable (5,500 LM)	62
PRC-FO20	Manufacture / supply - Outdoor 48-core FO cable - DAS (5,500 LM)	36
PRC-DSS20	Manufacture / supply - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-CND50	Delivery to site (Heet) - Steel & rigid conduits	80
PRC-MRK50	Delivery to site (Heet) - Marker posts, warning tape & route markers	244
PRC-HH50	Delivery to site (Heet) - Handholes & manholes (precast)	73
PRC-CLS30	Shipping / import - FO closures, splice trays, connectors & pigtails	69
PRC-COM30	Shipping / import - Communication modules & SIM hardware	187
PRC-CLD10	Place PO & supplier kick-off - Local-cloud hardware & licences (KSA...	85
PRC-CLS40	Customs clearance & SABER conformity - FO closures, splice trays, c...	69
PRC-TDRC30	Shipping / import - TDR coaxial cable (5,500 LM)	62
PRC-WX30	Shipping / import - Weather station sensors	175
PRC-COM40	Customs clearance & SABER conformity - Communication modules & SIM ...	187
PRC-CLS50	Delivery to site (Heet) - FO closures, splice trays, connectors & p...	69
PRC-FO30	Shipping / import - Outdoor 48-core FO cable - DAS (5,500 LM)	36
PRC-COM50	Delivery to site (Heet) - Communication modules & SIM hardware	187
PRC-CLD20	Manufacture / supply - Local-cloud hardware & licences (KSA hosted)	124
PRC-TDRC40	Customs clearance & SABER conformity - TDR coaxial cable (5,500 LM)	62
PRC-WX40	Customs clearance & SABER conformity - Weather station sensors	175
PRC-TDRC50	Delivery to site (Heet) - TDR coaxial cable (5,500 LM)	62
PRC-WX50	Delivery to site (Heet) - Weather station sensors	175
PRC-FO40	Customs clearance & SABER conformity - Outdoor 48-core FO cable - D...	36
PRC-PWR30	Shipping / import - UPS (min. 4 h) & electrical panels	144
PRC-FO50	Delivery to site (Heet) - Outdoor 48-core FO cable - DAS (5,500 LM)	36
PRC-DSS30	Shipping / import - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-PWR40	Customs clearance & SABER conformity - UPS (min. 4 h) & electrical ...	144
PRC-PWR50	Delivery to site (Heet) - UPS (min. 4 h) & electrical panels	144
PRC-TDR30	Shipping / import - TDR system (interrogator, antenna & accessories)	132
PRC-CLD30	Shipping / import - Local-cloud hardware & licences (KSA hosted)	124
PRC-DSS40	Customs clearance & SABER conformity - DSS cable NZS-DSS-C02 (5,500...	0
PRC-CLD40	Customs clearance & SABER conformity - Local-cloud hardware & licen...	124
PRC-TDR40	Customs clearance & SABER conformity - TDR system (interrogator, an...	132
PRC-DSS50	Delivery to site (Heet) - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-CLD50	Delivery to site (Heet) - Local-cloud hardware & licences (KSA host...	124
PRC-TDR50	Delivery to site (Heet) - TDR system (interrogator, antenna & acces...	132

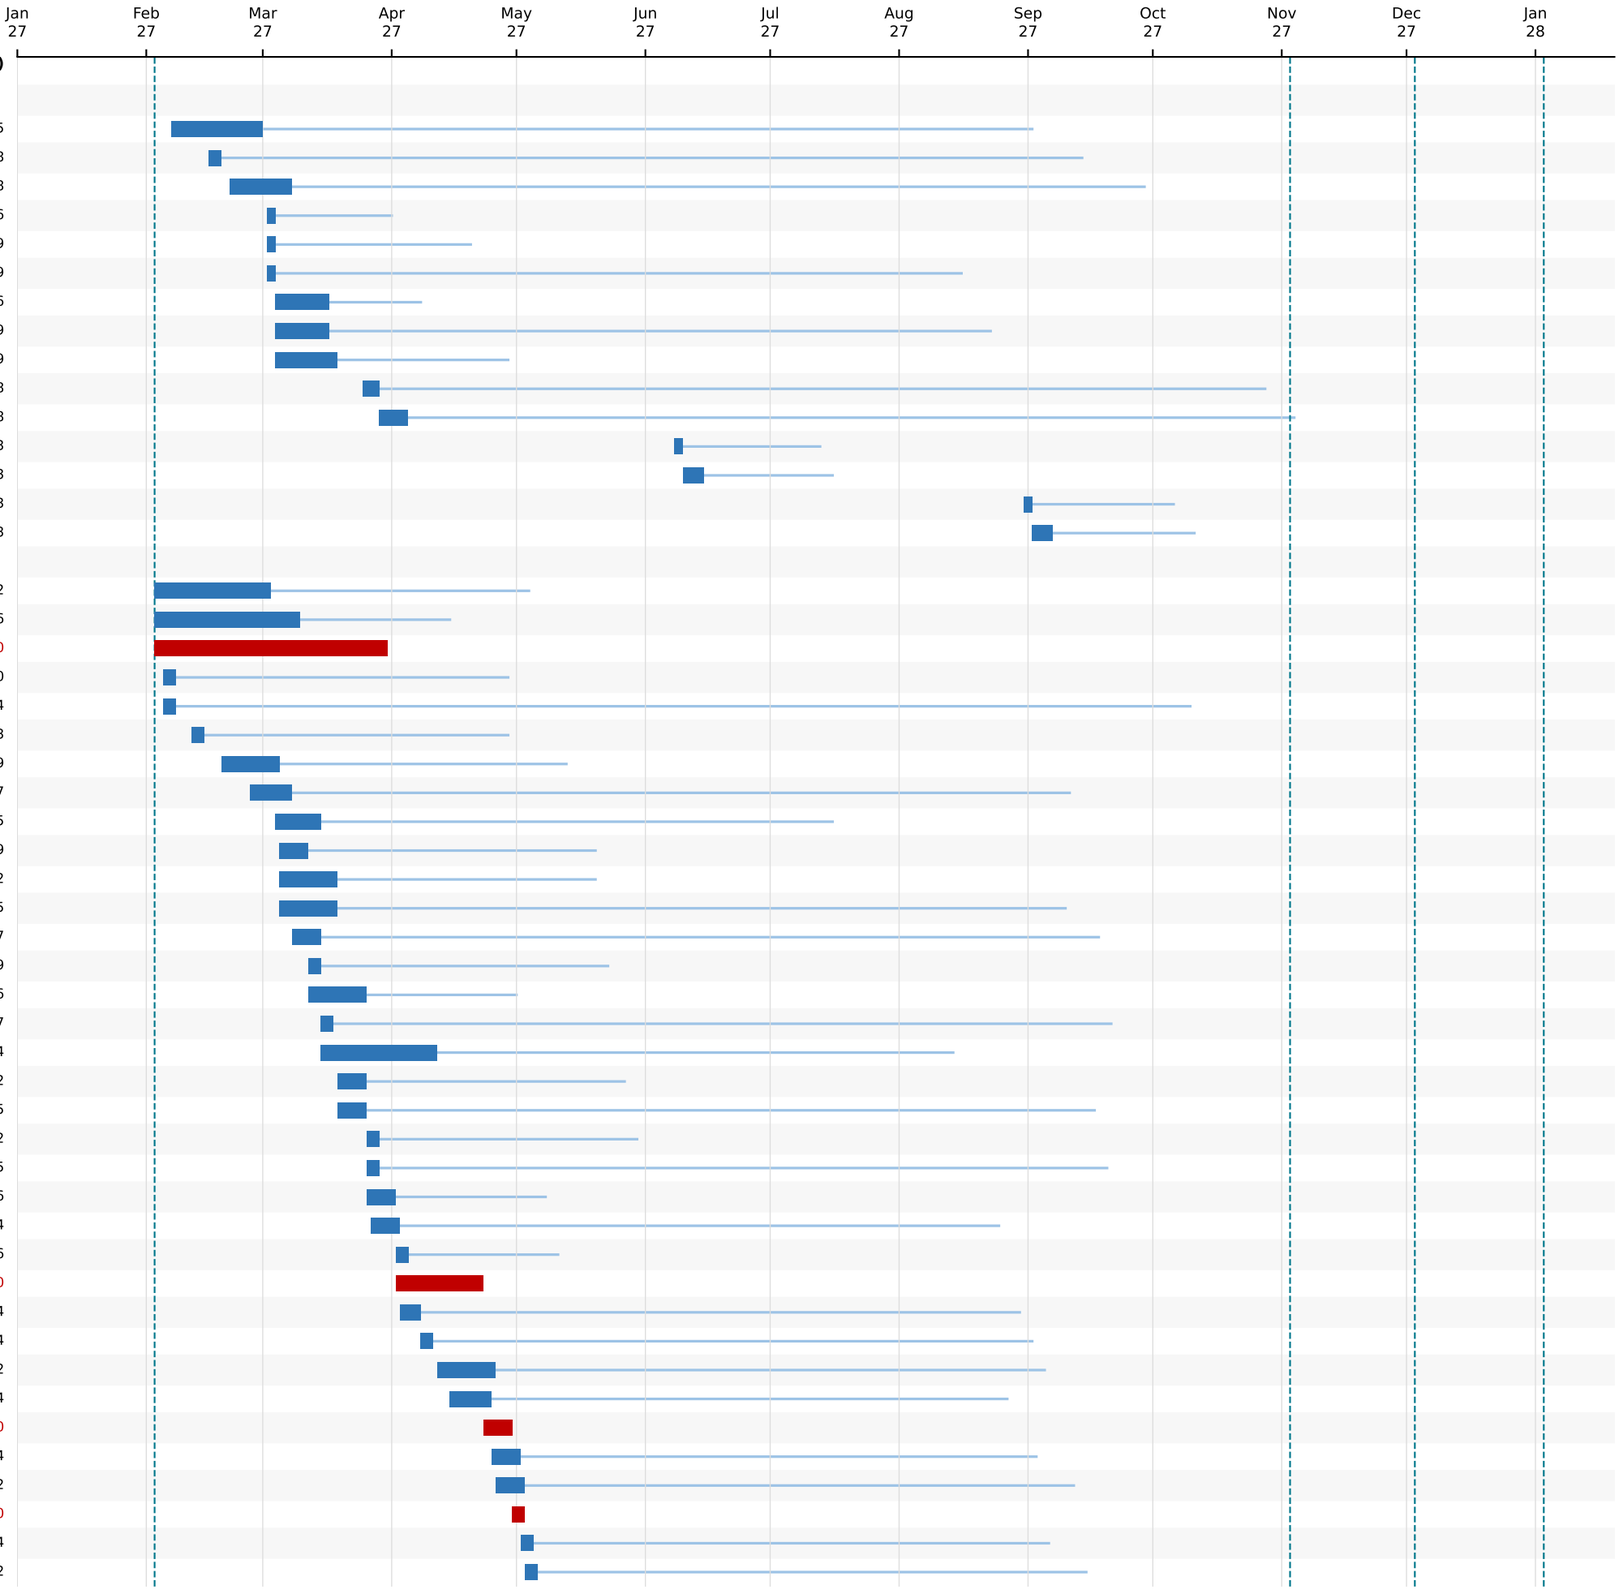


Critical path (TF = 0) · Non-critical (light line = total float) · Level of effort · Milestone · SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.3.8	**Factory Acceptance Testing (FAT)**	
FAT-COM	FAT at manufacturer - Communication modules & SIM hardware	187
FAT-TDRC	FAT at manufacturer - TDR coaxial cable (5,500 LM)	62
FAT-WX	FAT at manufacturer - Weather station sensors	175
FAT-FO	FAT at manufacturer - Outdoor 48-core FO cable - DAS (5,500 LM)	36
FAT-PWR	FAT at manufacturer - UPS (min. 4 h) & electrical panels	144
FAT-DSS	FAT at manufacturer - DSS cable NZS-DSS-C02 (5,500 LM)	0
FAT-TDR	FAT at manufacturer - TDR system (interrogator, antenna & accessori...	132
FAT-CLD	FAT at manufacturer - Local-cloud hardware & licences (KSA hosted)	124
1.3.9.1	**Section 1**	
CIV-110	Section 1 - excavate trench (800x200 mm) & sweet-sand bedding, 1,10...	16
CIV-120	Section 1 - handholes / manholes installation	16
CIV-130	Section 1 - steel & rigid conduits at culverts / track crossings	16
CAB-110	Section 1 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-120	Section 1 - backfill & compaction - layer 1	0
CAB-130	Section 1 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-110	Section 1 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-140	Section 1 - backfill & compaction - layer 2	0
CAB-150	Section 1 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-160	Section 1 - final backfill, compaction & reinstatement	0
CIV-140	Section 1 - marker posts, warning tape & route markers	89
1.3.9.2	**Section 2**	
CIV-210	Section 2 - excavate trench (800x200 mm) & sweet-sand bedding, 1,10...	26
CIV-220	Section 2 - handholes / manholes installation	26
CIV-230	Section 2 - steel & rigid conduits at culverts / track crossings	26
CAB-210	Section 2 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-220	Section 2 - backfill & compaction - layer 1	0
CAB-230	Section 2 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-210	Section 2 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-240	Section 2 - backfill & compaction - layer 2	0
CAB-250	Section 2 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-260	Section 2 - final backfill, compaction & reinstatement	0
CIV-240	Section 2 - marker posts, warning tape & route markers	69
1.3.9.3	**Section 3**	
CIV-310	Section 3 - excavate trench (800x200 mm) & sweet-sand bedding, 1,10...	8
CIV-320	Section 3 - handholes / manholes installation	8
CIV-330	Section 3 - steel & rigid conduits at culverts / track crossings	8
CAB-310	Section 3 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-320	Section 3 - backfill & compaction - layer 1	0
CAB-330	Section 3 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-310	Section 3 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-340	Section 3 - backfill & compaction - layer 2	0
CAB-350	Section 3 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-360	Section 3 - final backfill, compaction & reinstatement	0
CIV-340	Section 3 - marker posts, warning tape & route markers	49

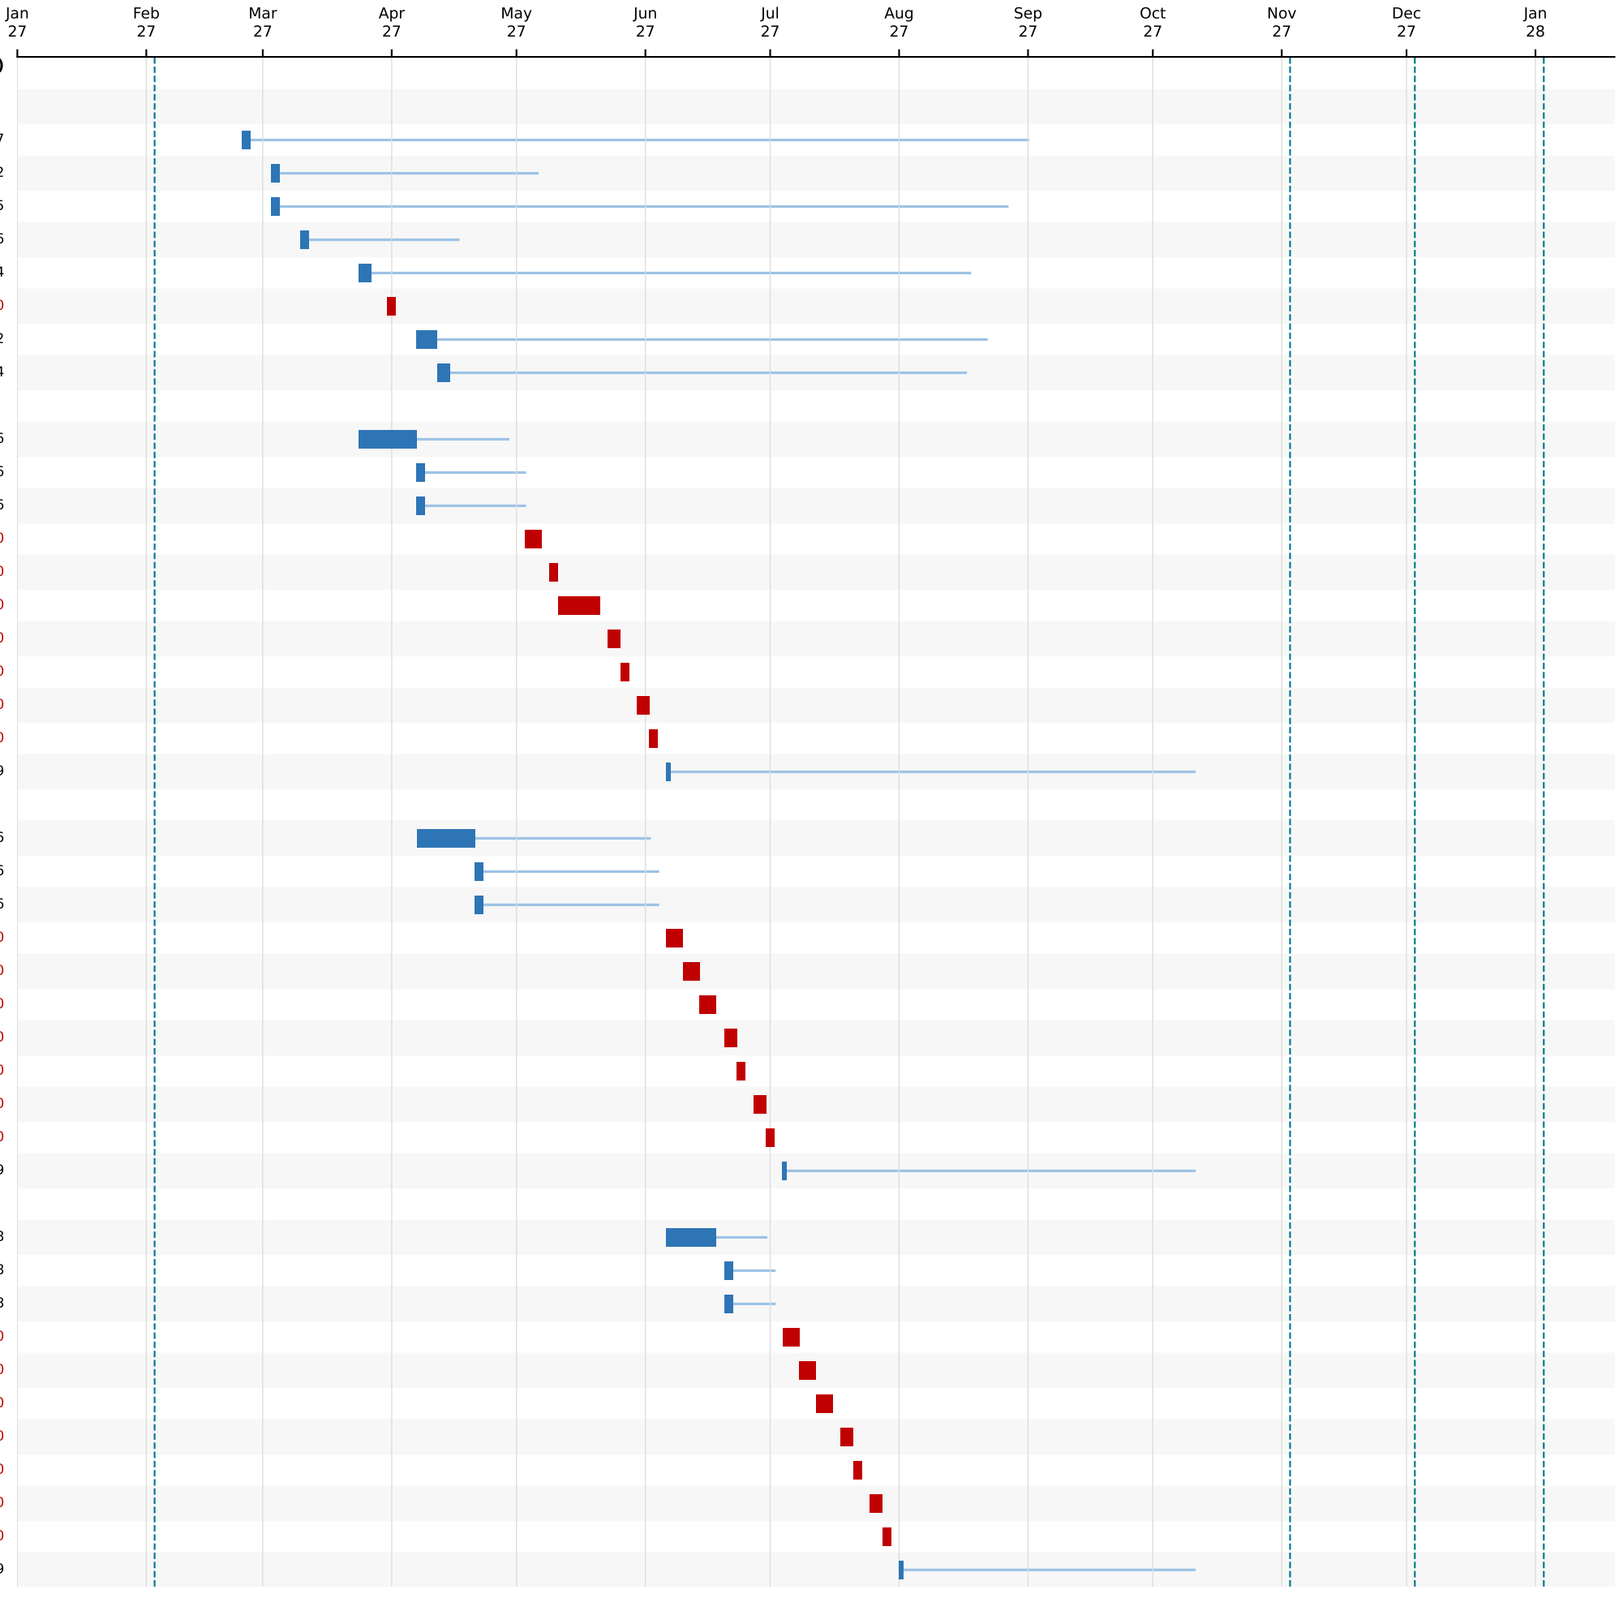


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
1.3.9.4	**Section 4**	
CIV-410	Section 4 - excavate trench (800x200 mm) & sweet-sand bedding, 1,10...	8
CIV-420	Section 4 - handholes / manholes installation	8
CIV-430	Section 4 - steel & rigid conduits at culverts / track crossings	8
CAB-410	Section 4 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-420	Section 4 - backfill & compaction - layer 1	0
CAB-430	Section 4 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-410	Section 4 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-440	Section 4 - backfill & compaction - layer 2	0
CAB-450	Section 4 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-460	Section 4 - final backfill, compaction & reinstatement	0
CIV-440	Section 4 - marker posts, warning tape & route markers	29
1.3.9.5	**Section 5**	
CIV-510	Section 5 - excavate trench (800x200 mm) & sweet-sand bedding, 1,10...	8
CIV-520	Section 5 - handholes / manholes installation	8
CIV-530	Section 5 - steel & rigid conduits at culverts / track crossings	8
CAB-510	Section 5 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-520	Section 5 - backfill & compaction - layer 1	0
CAB-530	Section 5 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-510	Section 5 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-540	Section 5 - backfill & compaction - layer 2	0
CAB-550	Section 5 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-560	Section 5 - final backfill, compaction & reinstatement	7
CIV-540	Section 5 - marker posts, warning tape & route markers	9
1.3.10	**Station Power, Shelter, Systems, Cloud & Cyber Installation**	
SHL-3410	Shelter expansion - civil works (if required per assessment)	104
PWR-3420	Electrical installation - panels & power upgrade (incl. SEC connect...	100
PWR-3430	UPS installation & 4-hour autonomy test	100
COM-3710	Communication modules installation	104
WX-3610	Weather station sensors installation	103
COM-3720	SIM activation, alert & e-mail distribution configuration	104
WX-3620	Weather station integration with data logger	103
CLD-3810	Local KSA cloud infrastructure - provisioning & set-up	84
TDR-3510	TDR system installation - interrogator & antenna	90
CLD-3820	Local KSA cloud infrastructure - hardening & connectivity	84
CYB-3920	Cybersecurity controls implementation & hardening	99
TDR-3520	TDR configuration, calibration & pre-commissioning	0
INT-4010	Integration with existing system & iSiteCentral - interfaces & data...	0
1.3.11	**Testing, Commissioning & Validation**	
TST-110	Section 1 - final OTDR certification & test record	87
CYB-3930	Third-party cybersecurity audit	99
CYB-3940	Audit findings closure & verification	99
TST-210	Section 2 - final OTDR certification & test record	67
TST-310	Section 3 - final OTDR certification & test record	47
TST-410	Section 4 - final OTDR certification & test record	27
TST-510	Section 5 - final OTDR certification & test record	7
TST-4110	Full-route OTDR certification report & as-installed test records	7

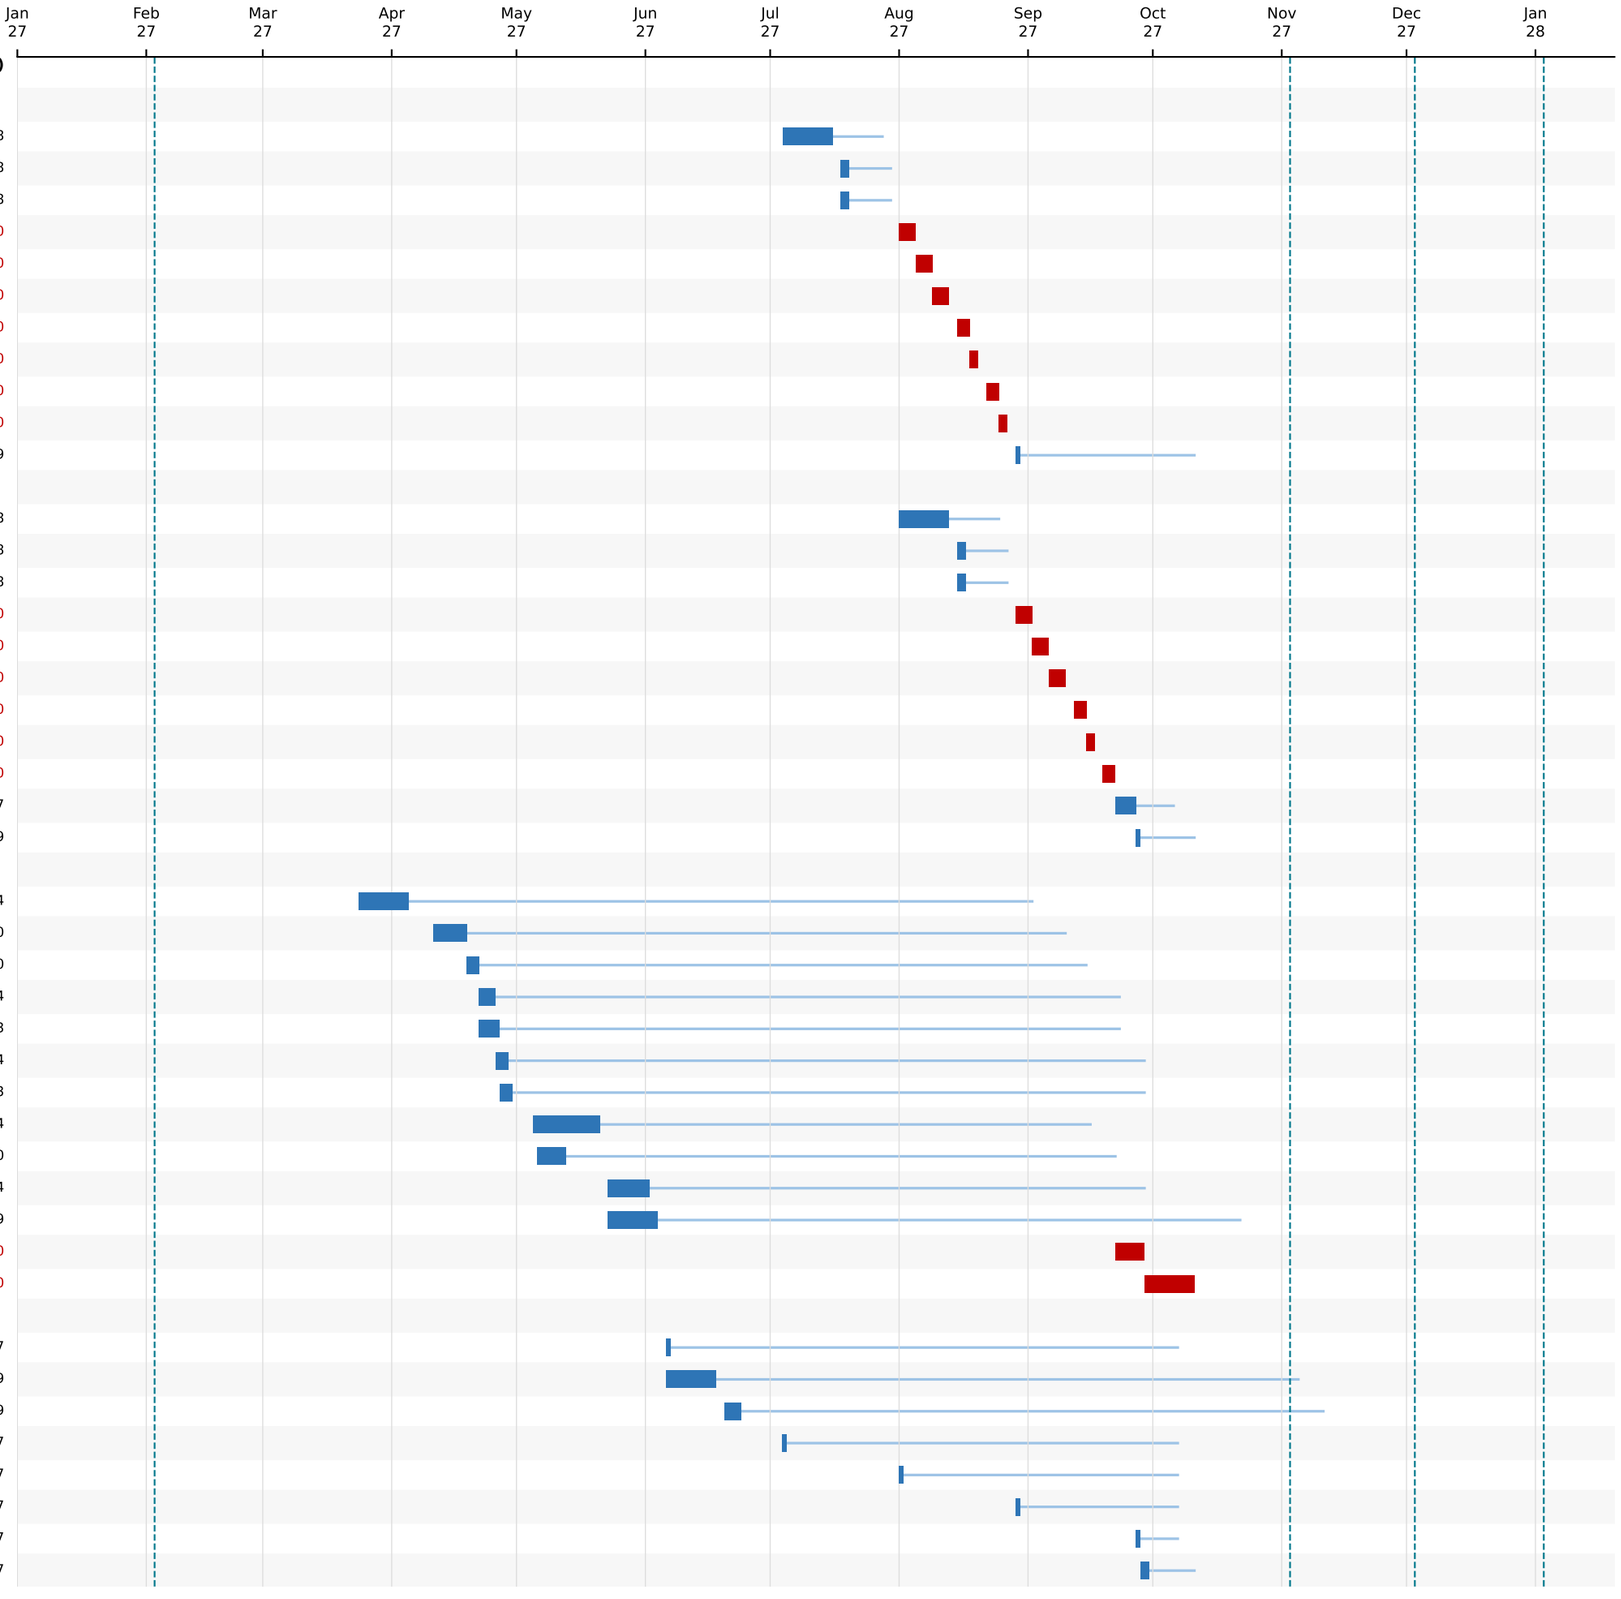


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Baseline Schedule - Detail

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
	1.3.13 Schedule Contingency (Time-Risk Allowance)	
CNT-0100	Schedule contingency - time-risk allowance (supplier, weather, Eid-...	0
	1.4.1 Management & Mobilization	
DEM-5100	Demobilization & site clearance	16
	1.4.11 Testing, Commissioning & Validation	
INT-4020	End-to-end integration test with existing system & iSiteCentral (pa...	0
TST-4210	SAT - site acceptance tests (sensors, power, communications, operat...	0
CMS-4310	System commissioning & calibration - DAS, DSS, TDR & weather station	0
CMS-4320	Trial operation - baseline data collection & performance validation	0
	1.4.12 Documentation, Training & Handover	
DOC-5040	User training for SAR staff (5 days)	21
DOC-5020	As-built drawings (3 sets, hard + soft) - final revision after SAT	10
DOC-5030	O&M manuals (3 sets) - final revision	10
DOC-5010	Technical reports - TDR, DAS (seismic), DSS strain, weather data & ...	0
	1.5.2 Submittals (Contractor)	
DOC-5050	Handover dossier - QA/QC, material test & HSE records, reports - co...	0
SUB-5070	Address SAR comments & resubmit dossier	0
	1.5.3 SAR Reviews & Approvals	
APR-5060	SAR review of handover dossier (as-builts, O&M, reports)	0
APR-5080	SAR final acceptance of handover dossier	0
	1.5.12 Documentation, Training & Handover	
HND-5090	Formal handover & Taking-Over certificate (SAR)	0
	1.6 Post-Completion - Defects Liability Period (DLP)	
DLP-9010	Start of Defects Liability Period (DLP)	0
DLP-9020	Defects liability support (12 months after Taking-Over)	0
DLP-9030	End of Defects Liability Period	0

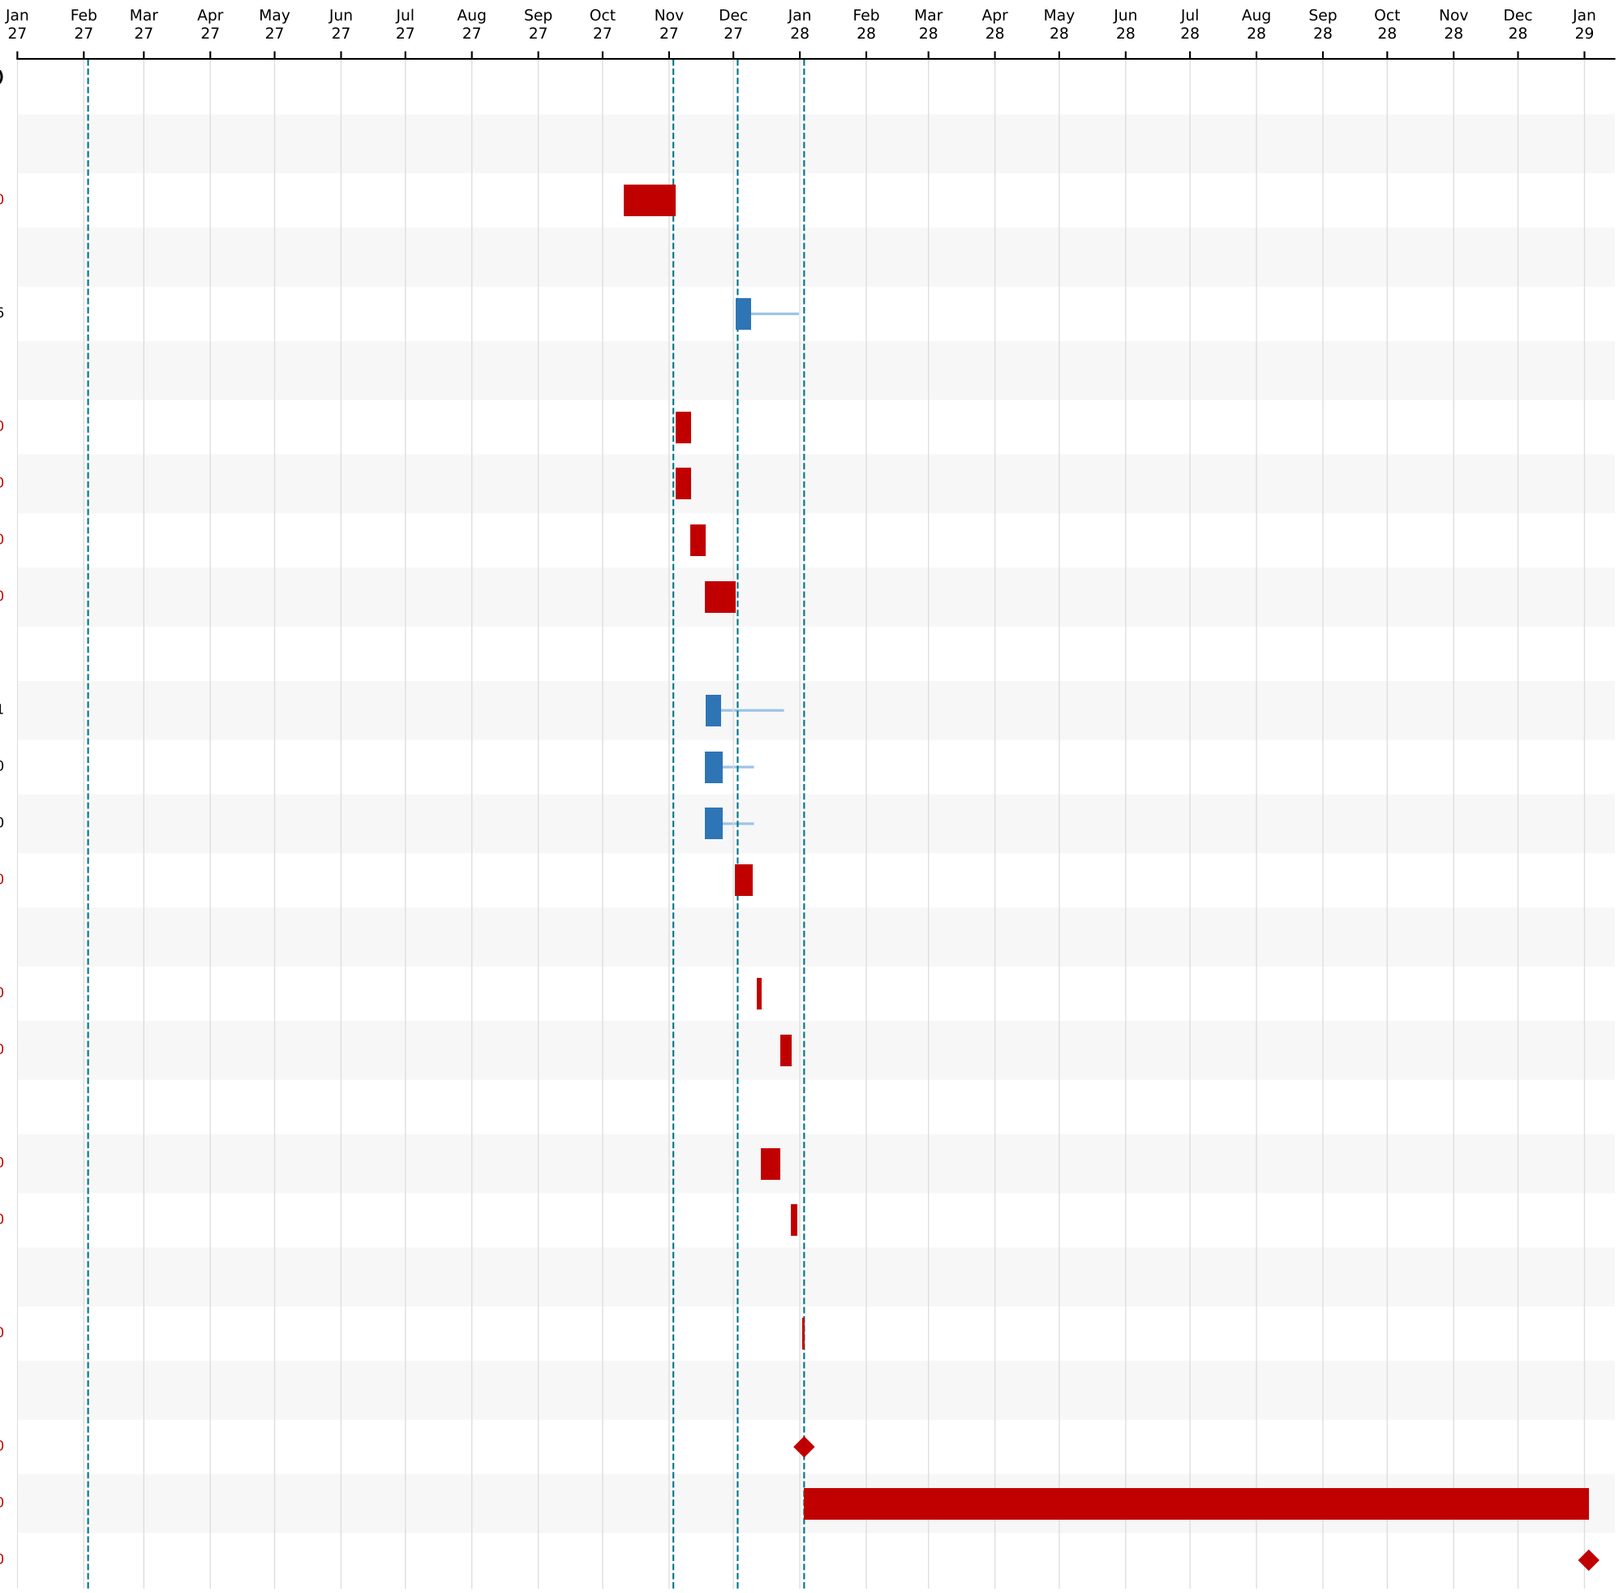


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Critical Path - longest path, total float = 0

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
MS-001	NTP - Notice to Proceed (assumed date; re-base on actual NTP)	0
MOB-1010	Kick-off meeting & project management set-up	0
SUB-1430	Material submittal - DSS cable NZS-DSS-C02, 48-core FO cable, TDR c...	0
APR-1530	SAR review - cable materials (DSS, FO, TDR coax)	0
SUB-1535	Address SAR comments & resubmit cable materials	0
APR-1536	SAR final approval - cable materials	0
PRC-DSS10	Place PO & supplier kick-off - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-DSS20	Manufacture / supply - DSS cable NZS-DSS-C02 (5,500 LM)	0
FAT-DSS	FAT at manufacturer - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-DSS30	Shipping / import - DSS cable NZS-DSS-C02 (5,500 LM)	0
PRC-DSS40	Customs clearance & SABER conformity - DSS cable NZS-DSS-C02 (5,500...	0
PRC-DSS50	Delivery to site (Heet) - DSS cable NZS-DSS-C02 (5,500 LM)	0
CAB-110	Section 1 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-120	Section 1 - backfill & compaction - layer 1	0
CAB-130	Section 1 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-110	Section 1 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-140	Section 1 - backfill & compaction - layer 2	0
CAB-150	Section 1 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-160	Section 1 - final backfill, compaction & reinstatement	0
CAB-210	Section 2 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-220	Section 2 - backfill & compaction - layer 1	0
CAB-230	Section 2 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-210	Section 2 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-240	Section 2 - backfill & compaction - layer 2	0
CAB-250	Section 2 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-260	Section 2 - final backfill, compaction & reinstatement	0
CAB-310	Section 3 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-320	Section 3 - backfill & compaction - layer 1	0
CAB-330	Section 3 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-310	Section 3 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-340	Section 3 - backfill & compaction - layer 2	0
CAB-350	Section 3 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-360	Section 3 - final backfill, compaction & reinstatement	0
CAB-410	Section 4 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-420	Section 4 - backfill & compaction - layer 1	0
CAB-430	Section 4 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-410	Section 4 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-440	Section 4 - backfill & compaction - layer 2	0
CAB-450	Section 4 - Layer 3: lay TDR coaxial cable, continuity test	0
CAB-460	Section 4 - final backfill, compaction & reinstatement	0
CAB-510	Section 5 - Layer 1: lay DSS cable, pre-installed connectors, OTDR ...	0
CAB-520	Section 5 - backfill & compaction - layer 1	0
CAB-530	Section 5 - Layer 2: pull 48-core FO cable (DAS), OTDR test	0
SPL-510	Section 5 - fusion splicing (<=0.1 dB), FO closures & OTDR splice-l...	0
CAB-540	Section 5 - backfill & compaction - layer 2	0
CAB-550	Section 5 - Layer 3: lay TDR coaxial cable, continuity test	0
TDR-3520	TDR configuration, calibration & pre-commissioning	0
INT-4010	Integration with existing system & iSiteCentral - interfaces & data...	0
MS-070	Stage 2 complete - procurement, construction & installation complete	0
CNT-0100	Schedule contingency - time-risk allowance (supplier, weather, Eid-...	0

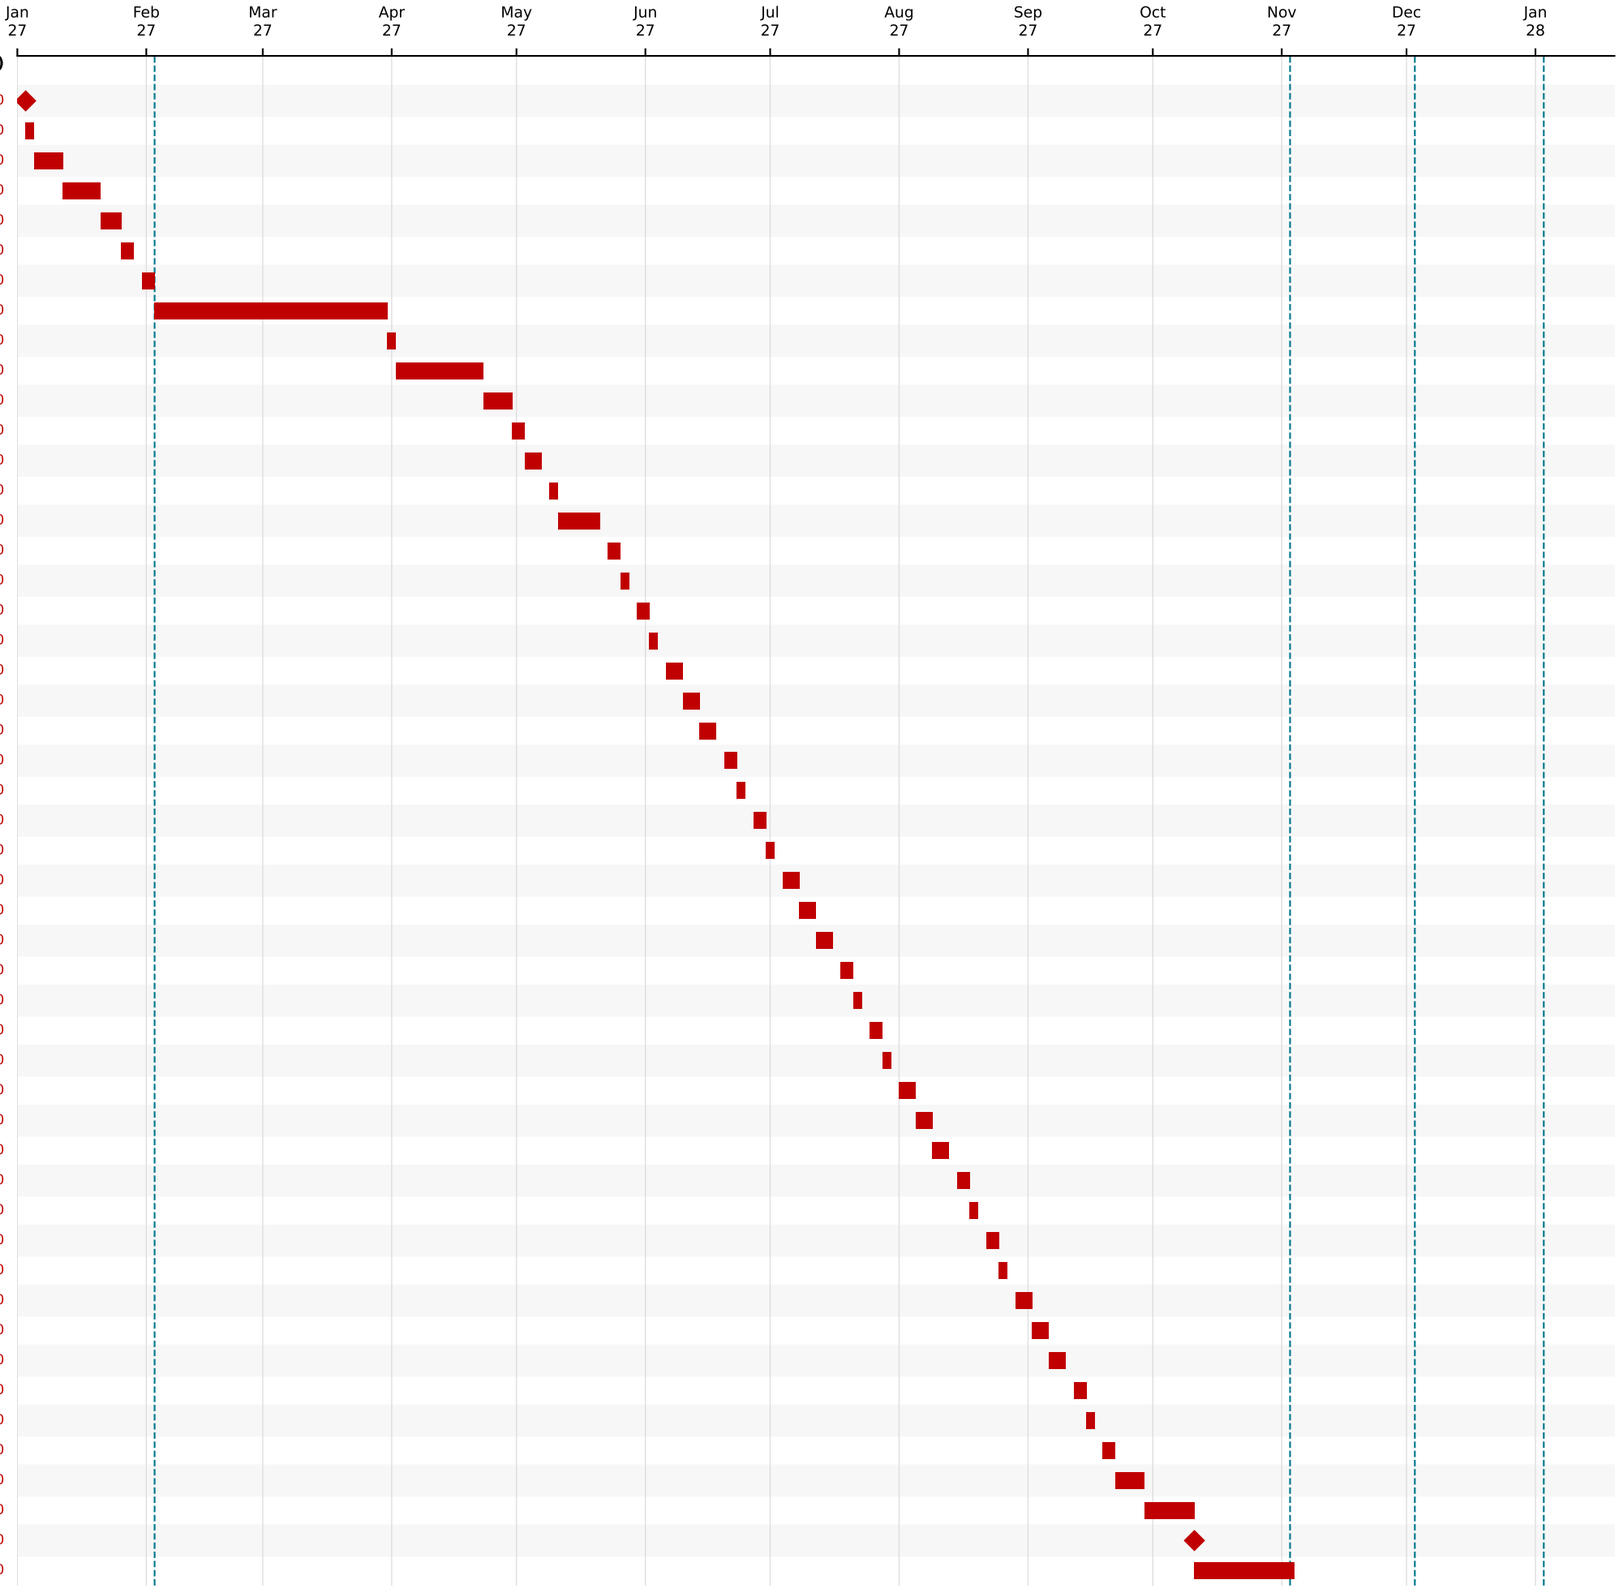


Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)

Critical Path - longest path, total float = 0

Extension of the Existing Rail Monitoring System in HEET - Baseline Rev 01 (data date 03-Jan-27) - NTP assumed 03-Jan-27, Contract Completion 02-Jan-28 - Total float on critical path = 0

Activity ID	Activity Name	TF (wd)
TST-4210	SAT - site acceptance tests (sensors, power, communications, operat...	0
INT-4020	End-to-end integration test with existing system & iSiteCentral (pa...	0
MS-080	SAT complete (incl. integration tests & cyber audit closure)	0
CMS-4310	System commissioning & calibration - DAS, DSS, TDR & weather station	0
CMS-4320	Trial operation - baseline data collection & performance validation	0
MS-100	Stage 3 complete - commissioning & performance validation complete	0
DOC-5010	Technical reports - TDR, DAS (seismic), DSS strain, weather data & ...	0
DOC-5050	Handover dossier - QA/QC, material test & HSE records, reports - co...	0
APR-5060	SAR review of handover dossier (as-builts, O&M, reports)	0
SUB-5070	Address SAR comments & resubmit dossier	0
APR-5080	SAR final acceptance of handover dossier	0
HND-5090	Formal handover & Taking-Over certificate (SAR)	0
MS-120	Taking-Over - CONTRACT COMPLETION (12 months from NTP)	0
DLP-9010	Start of Defects Liability Period (DLP)	0
DLP-9020	Defects liability support (12 months after Taking-Over)	0
DLP-9030	End of Defects Liability Period	0

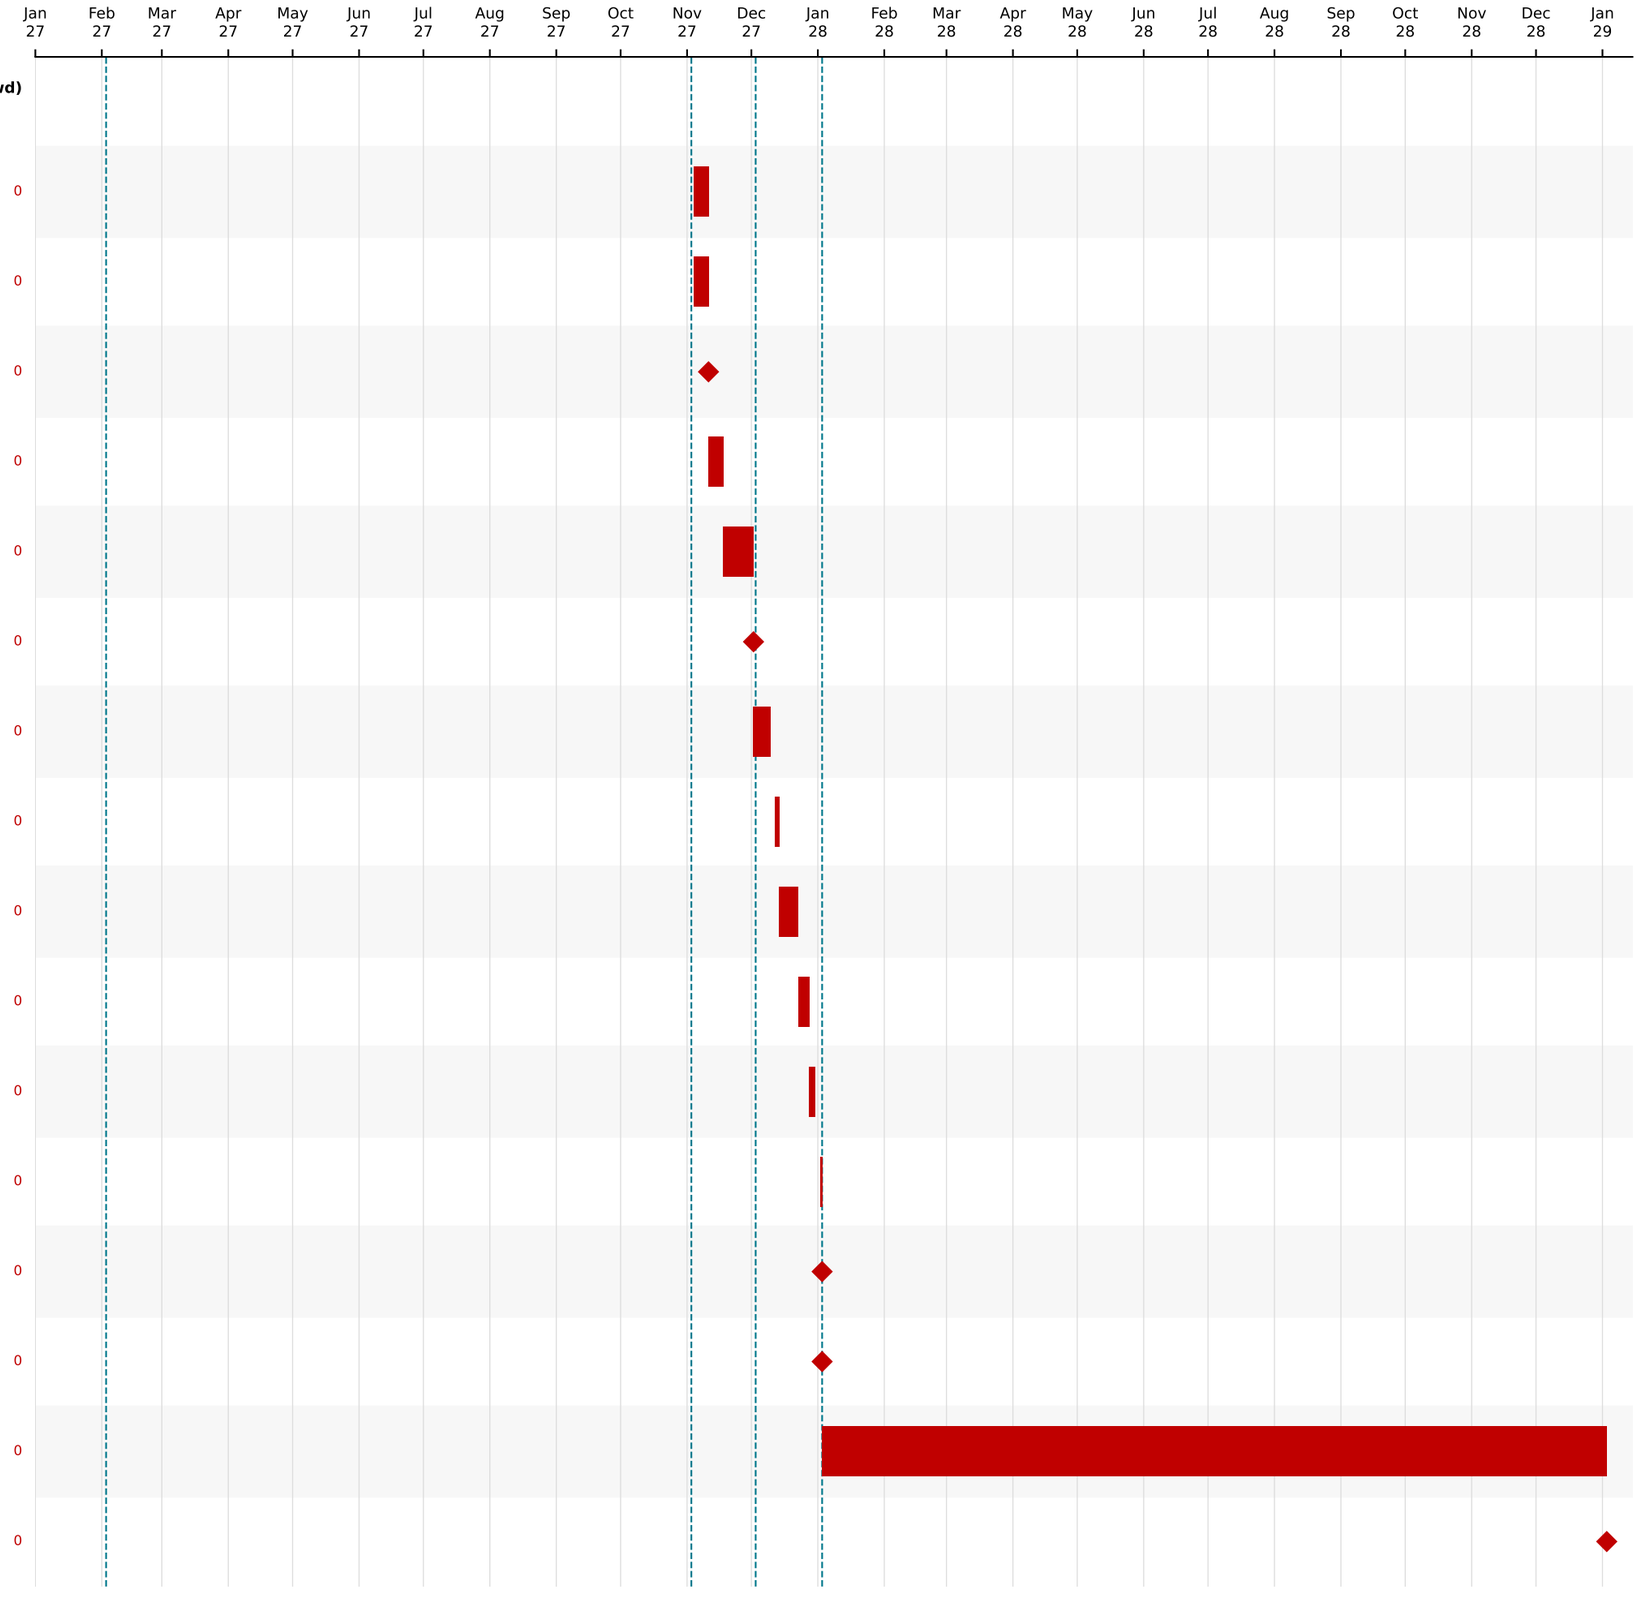

Critical path (TF = 0) | Non-critical (light line = total float) | Level of effort | Milestone | SoW stage ends (2-Feb, 2-Nov, 2-Dec-27, 2-Jan-28)
